

Burndown Chart Reflection

Burndown chart

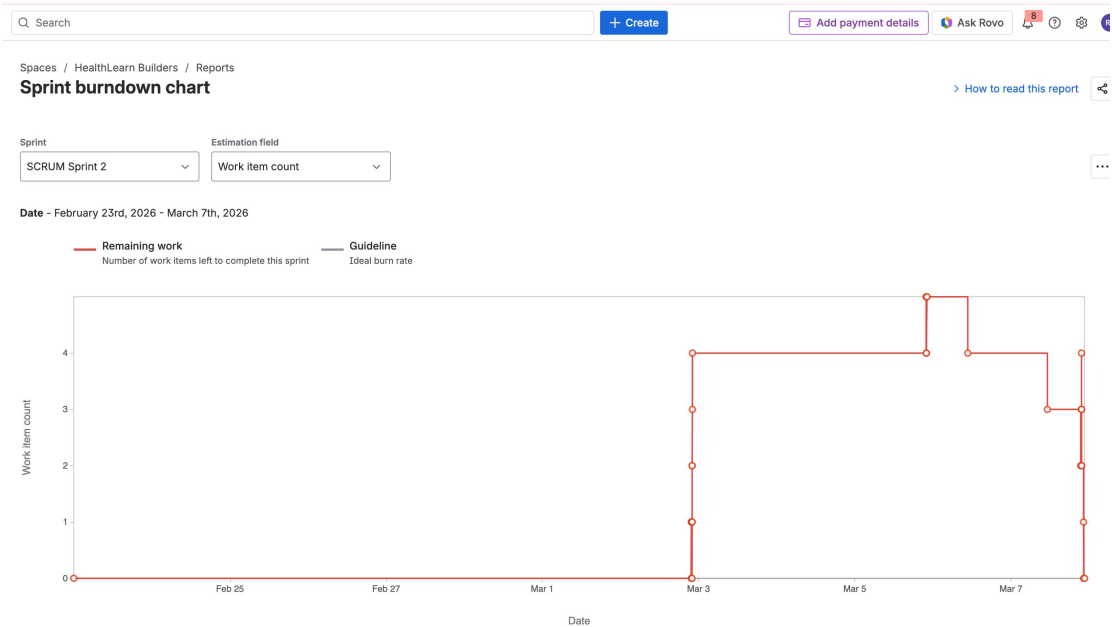


Chart for Sprint2

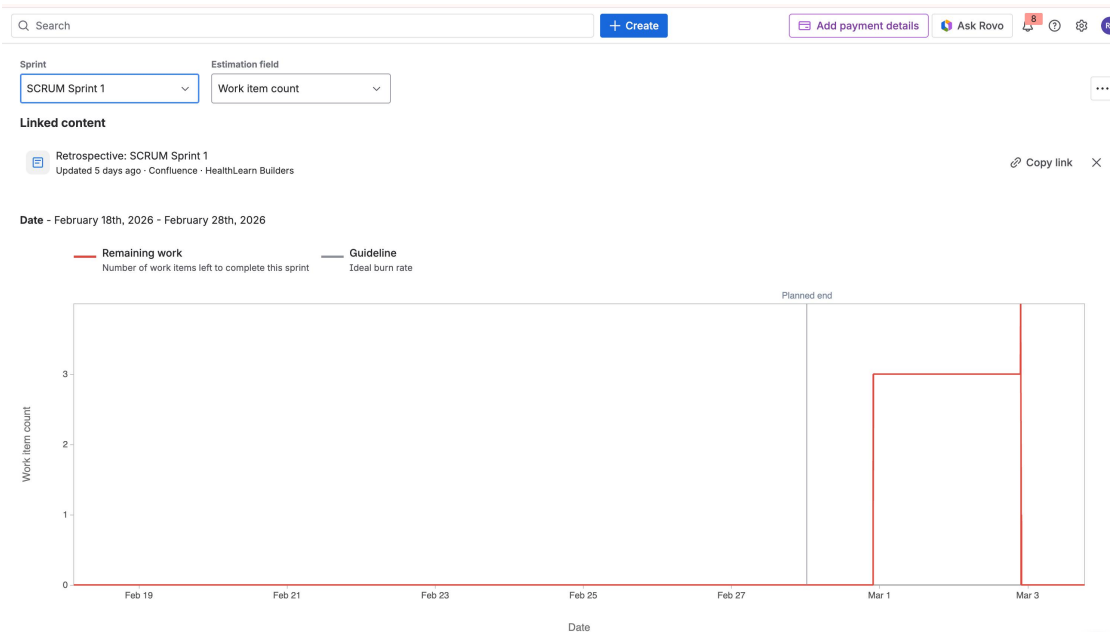


Chart for sprint1

Note on Burndown Chart Visualization

Before discussing the burndown results, we would like to clarify an issue with the visualization. At the beginning of the project, our team did not assign story points to the user stories in Jira. As a result, the burndown chart cannot properly display the expected burn-

down timeline based on story points. Instead, the chart only tracks work item count, which limits the accuracy of velocity and progress visualization.

This situation was communicated in advance to TA Anna and the course instructor, and they acknowledged the issue and expressed understanding that the burndown chart may not fully reflect sprint progress in the intended format.

Sprint Velocity vs Previous Sprint

Comparing Sprint 2 with Sprint 1, the team's velocity shows moderate improvement in terms of task completion and workflow coordination.

In Sprint 1, the team spent significant time setting up the project environment, clarifying requirements, and organizing the development workflow. As a result, a portion of the sprint was dedicated to project preparation rather than completing implementation tasks. The burndown chart for Sprint 1 shows that most tasks were completed near the end of the sprint, indicating that work distribution was not evenly spread across the timeline.

In Sprint 2, the team had a clearer understanding of the system architecture and project requirements. This allowed members to focus more directly on implementation tasks such as improving the admin portal, fixing email verification for user registration, and working on integration testing for appointment services and therapist dashboards.

Although tasks were still completed in clusters rather than steadily across the sprint, the team demonstrated better coordination and a clearer division of responsibilities compared to Sprint 1.

Overall, Sprint 2 shows improved team alignment and task execution, though the burndown pattern indicates that task completion still tends to occur toward the later part of the sprint.

Changes and Reasons

Several changes occurred during Sprint 2 that influenced the burndown chart and sprint progress.

First, new tasks were added during the sprint. For example, additional work items related to improving the patient dashboard entry points and fixing functionality issues were introduced after the sprint had already started. These scope adjustments caused the remaining work line in the burndown chart to temporarily increase.

Second, some tasks required additional clarification after discussions with the project founder. As a result, certain user stories were refined or reorganized in Jira to better reflect the expected functionality. This led to adjustments in task allocation and occasionally delayed task completion.

Third, the team spent time improving Jira management and workflow organization, including standardizing user story descriptions and acceptance criteria. While this work does not directly reduce remaining tasks in the burndown chart, it helped improve task clarity and coordination among team members.

These changes reflect the natural iteration process of agile development, where requirements may evolve and tasks are refined as the team gains a deeper understanding of the system.
